


Notice Number:	050- 2025
Issue Date:	15/12/2025
This notice will be updated and issued weekly, giving information of any operations carried out in relation to East Anglia THREE offshore windfarm in the previous 7 days and any ongoing/planned operations for the next 7 days. Any notice to mariners issued by East Anglia THREE are available on Scottish Power Renewables website www.scottishpowerrenewables.com and the Kingfisher bulletin https://kingfisherbulletin.org/	

Weekly Notice of Operations

Prepared by:	Checked by:	Approved by:
Marine Coordinator	Lead Marine Coordinator	Offshore installation Manager

1. PROJECT INTRODUCTION

East Anglia THREE will be a large offshore wind farm, located 69 km off the Norfolk coast. With a projected capacity of approximately 1400MW, the wind farm shall supply electricity to approximately one million UK homes. Onshore construction for the project started in July 2022. Offshore construction has commenced.

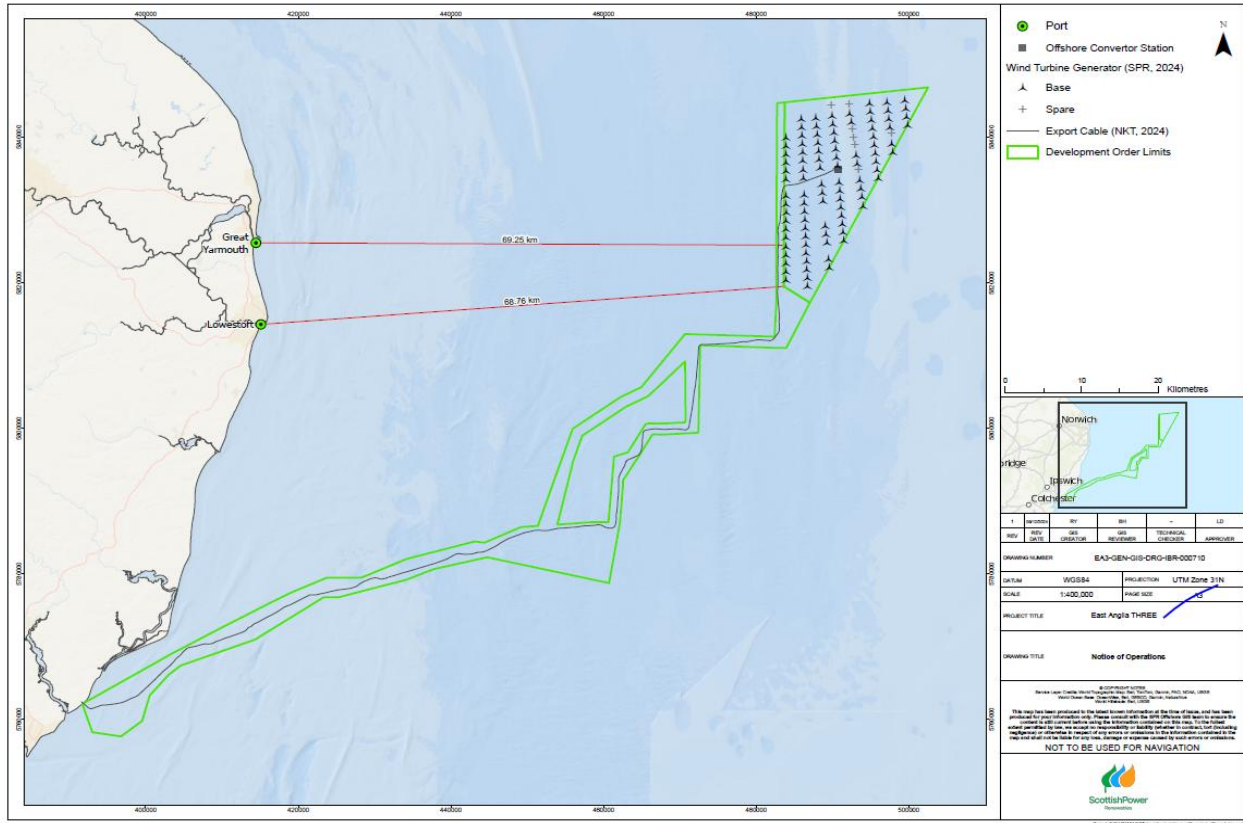

2. SUMMARY OF NOTICE TO MARINERS

EA3 NTM (Notice to Mariners) Tracker

NTM No*	NTM Name	Start Date	End Date	Status	Comments/Workscope	Distribution Date (open)
048/2024	Commencement of Construction of EA3 OWF	01/11/2024	N/A	Open	EA3 OWF Construction	25/10/2024
005/2025	Maintenance and Redeployment of EA3 Weather Buoy	22/01/2025	N/A	Open	Maintenance of EA3 Weather Buoy	22/01/2025
009/2025	Notification of Guard Vessel	01/03/2025	N/A	Open	Guard Vessel	19/02/2025
012/2025	Monopile and Transition Piece Installation Campaign	27/03/2025	Q1 2026	Open	Monopile and TP Installation Campaign	14/03/2025
017/2025	CTV Rebellion	04/01/2025	TBC	Open	CTV Operations	26/03/2025
020/2025	MP TP Bolting And Grouting	25/04/2025	TBC	Open	MP TP Bolting And Grouting	04/07/2025
024/2025	Confirmed Unexploded Ordnance	30/04/2025	TBC	Open	cUXO	30/04/2025
036/2025	Wave Rider Buoy	12/06/2025	TBC	Open	Wave Rider Buoy	12/06/2025
050/2025	CTV NR Hunter	07/08/2025	TBC	Open	CTV NR Hunter	11/08/2025
053/2025	Export Cable Installation	26/08/2025	TBC	Open	Export Cable Installation	24/08/2025
064/2025	Marine Mammal Monitoring - Passive Acoustic Monitoring Stations	10/10/2025	31/10/2027	Open	PAM Stations	10/10/2025
065/2025	Export Cable Guard Vessel	20/05/2025	TBC	Open	Export Cable Guard Vessels	17/10/2025
067/2025	CTV NR Predator	28/10/2025	TBC	Open	CTV NR Predator	29/10/2025
069/2025	Esvagt Cobra (OFCS ERRV)	03/11/2025	TBC	Open	Esvagt Cobra (OFCS ERRV)	29/10/2025
072/2025	Bos Prelude	04/11/2025	TBC	Open	OFCS Platform Supply Vessel	29/10/2025
073/2025	Post-lay mattress installation	09/11/2025	TBC	Open	Post-Lay Mattress Installation	09/11/2025
076/2025	Esvagt Carpathia (OFCS ERRV)	12/11/2025	TBC	Open	Esvagt Carpathia (OFCS ERRV)	12/11/2025
077/2025	Pre-Installation Survey Campaign 3	01/12/2025	TBC	Open	Pre-Installation Survey Campaign Three	17/11/2025
078/2025	Windea Clausius (OFCS Platform Commissioning Service Operation Vessel)	24/11/2025	TBC	Open	OFCS Commissioning	18/11/2025
079/2026	Maintenance of EA3 Weather Buoys	28/11/2025	TBC	Open	Maintenance of EA3 Weather Buoy	19/11/2025
080/2025	Aids To Navigation Demarcation Buoys	28/11/2025	TBC	Open	Demarcation Buoys	28/11/2025
081/2025	(OFCS) Jack up barge	02/12/2025	TBC	Open	OFCS Jack up barge	02/12/2025

2.1. AIDS TO NAVIGATION STATUS

The following aids to navigation are deployed within the East Anglia THREE offshore windfarm:

Buoy Type	ID	Deployed Latitude	Deployed Longitude	Buoy Characteristic
EA3 North 1 Buoy	N1	52° 45.472'N	002° 50.962'E	• Pillar shaped with a North cardinal shaped top mark • Quick Flashing Light Character
EA3 North 2 Buoy	N2	52° 45.917'N	003° 00.151'E	• Pillar shaped with a North cardinal shaped top mark • Very Quick Flashing Light Character
EA3 East 1 Buoy	E1	52° 44.254'N	003° 00.808'E	• Pillar shaped with an East cardinal shaped top mark • Quick Flashing (3) 10s Light Character
EA3 East 2 Buoy	E2	52° 38.892'N	002° 56.569'E	• Pillar shaped with an East cardinal shaped top mark • Very Quick Flashing (3) 5s Light Character
EA3 East 3 Buoy	E3	52° 33.158'N	002° 51.632'E	• Pillar shaped with an East cardinal shaped top mark • Quick Flashing (3) 10s Light Character
EA3 South 1 Buoy	S1	52° 31.148'N	002° 48.252'E	• Pillar shaped with a South cardinal shaped top mark • Very Quick Flashing (6) +1 long flash 10s Light Character
EA3 West 1 Buoy	W1	52°31.814'N	002°45.153'E	• Pillar shaped with a West cardinal shaped top mark • Quick Flashing (9) 15s Light Character
EA3 West 2 Buoy	W2	52° 37.466'N	002°44.872'E	• Pillar shaped with a West cardinal shaped top mark • Very Quick Flashing (9) 10s Light Character
EA3 West 3 Buoy	W3	52°43.123'N	002°45.093'E	• Pillar shaped with a West cardinal shaped top mark • Quick Flashing (9) 15s Light Character
EA3 Special 1 Buoy	SP1	52° 45.708'N	002° 55.556'E	• Pillar shaped with a yellow 'X' shaped top mark • Flashing yellow 5s Light Character
EA3 Special 2 Buoy	SP2	52° 40.790'N	002° 59.023'E	• Pillar shaped with a yellow 'X' shaped top mark • Flashing yellow 5s Light Character
EA3 Special 3 Buoy	SP3	52° 36.130'N	002° 54.059'E	• Pillar shaped with a yellow 'X' shaped top mark • Flashing yellow 5s Light Character
EA3 Special 4 Buoy	SP4	52°34.642'N	002°45.165'E	• Pillar shaped with a yellow 'X' shaped top mark • Flashing yellow 5s Light Character
EA3 Special 5 Buoy	SP5	52°40.295'N	002°44.849'E	• Pillar shaped with a yellow 'X' shaped top mark • Flashing yellow 5s Light Character
EA3 Special 6 Buoy	SP6	52°44.640'N	002°47.484'E	• Pillar shaped with a yellow 'X' shaped top mark • Flashing yellow 5s Light Character
EA3 Weather Monitoring Buoy North	NWB	52°44.841'N	002°58.611'E	• Flash sequence – Fl (5) 20s. Amber light, 3nm visibility
EA3 Weather Monitoring Buoy South	SWB	52°32.880'N	002°46.961'E	• Flash sequence – Fl (5) 20s. Amber light, 3nm visibility
Wave Rider buoy	WRB	52°39.166'N	002°52.332'E	• Flashing (5) 20s. Yellow light, 4nm visibility.

For installed asset light characteristics see section [6](#).

3. WORKS CARRIED OUT IN THE LAST 7 DAYS

3.1. GV Tess

- **Guard Vessel:** GV Tess has continued guard vessel duties within the boundary of the East Anglia THREE Offshore Windfarm Array.

3.2. Norside Supporter

- **TP Completion Works:** Norside Supporter has continued with foundation completion operations within the East Anglia THREE boundary of the Offshore Windfarm Array, including bolt tensioning and grouting operations.
- **Port call:** Norside Supporter made a port call to Rotterdam on the 09/12/2025 to complete cargo operations before returning to the East Anglia THREE Offshore Windfarm Array.

3.3. Seaway Ventus

- **Monopile And Transition Piece Installation Campaign:** Seaway Ventus has continued with Monopile and Transition Piece Installation operations within the East Anglia THREE boundary of the Offshore Windfarm Array.
- **Port call:** Seaway Ventus made a port call to Vlissingen on the 13/12/2025 to complete loading operations and conduct a crew change.

3.4. GV Reul Na Mara

- **Export Cable Guard Vessel:** GV Reul Na Mara has continued with guard vessel duties along the East Anglia THREE export cable corridor.
- **Demobilisation:** GV Ruel Na Mara demobilised from the project on the 12/11/2025 in the port of Lowestoft.

3.5. GV Adventure

- **Export Cable Guard Vessel:** GV Adventure has continued with guard vessel duties along the East Anglia THREE export cable corridor.
- **Port call:** GV Adventure made a port call to Lowestoft on the 11/12/2025, before returning to the East Anglia THREE export cable corridor.

3.6. GV Arina

- **Export Cable Guard Vessel:** GV Arina has continued with guard vessel duties along the East Anglia THREE export cable corridor.
- **Port call:** GV Arina made a port call to Lowestoft on the 14/12/2025 to complete a crew change.

3.7. GV Resolution

- **Export Cable Guard Vessel:** GV Resolution has continued with guard vessel duties along the East Anglia THREE export cable corridor.

3.8. GV Renown

- **Export Cable Guard Vessel:** GV Renown has continued with guard vessel duties along the East Anglia THREE export cable corridor.
- **Demobilisation:** GV Renown demobilised from the project on the 13/11/2025 in the port of Lowestoft.

3.9. GV Accord

- **Export Cable Guard Vessel:** GV Accord has continued with guard vessel duties along the East Anglia THREE export cable corridor.

3.10. NR Rebellion

- **Crew Transfer Vessel:** NR Rebellion has continued with crew transfer duties within the East Anglia THREE boundary of the Offshore Windfarm Array and export cable corridor.

3.11. NR Hunter

- **Crew Transfer Vessel:** NR Hunter has continued with crew transfer duties within the East Anglia THREE boundary of the Offshore Windfarm Array and export cable corridor.

3.12. NR Predator

- **Crew Transfer Vessel:** NR Predator has completed crew transfer duties along the East Anglia THREE export cable corridor.

3.13. Esvagt Cobra

- **Emergency Response and Rescue Vessel:** Esvagt Cobra has returned to the East Anglia THREE boundary of the Offshore Windfarm Array to continue with emergency rescue and recovery support (ERRV).

3.14. Grand Canyon III

- **Rock-bag installation:** Grand Canyon III has continued with Rock Bag Installation operations within the East Anglia THREE boundary of the Offshore Windfarm Array.
- **Demobilisation:** Grand Canyon III completed operations and demobilised from the project in the port of Blyth on the 14/12/2025.

3.15. Flintstone

- **Subsea Rock installation:** Flintstone has continued with subsea rock installation operations along the East Anglia THREE export cable corridor.
- **Demobilisation:** Flintstone completed operations and demobilised from the project on the 14/12/2025 in the port of Mekjarvik.

3.16. Windea Clausius

- **OFCS Platform Commissioning Service Operation Vessel (SOV):** Windea Clausius has continued providing accommodation and Walk-To-Work access for the commissioning phase of the East Anglia THREE Offshore Converter Station.
- **Port call:** Windea Clausius made a port call to Ijmuiden on 08/12/2025 before returning to the East Anglia THREE boundary of the Offshore Windfarm Array.

3.17. Olympic Taurus

- **Post-Lay Mattress Installation:** Olympic Taurus has continued with post-lay mattress installation operations along the East Anglia THREE export cable corridor.

3.18. Bos Prelude

- **OFCS Platform Supply Vessel:** Bos Prelude has conducted cargo transfer operations within the East Anglia THREE boundary of the Offshore Windfarm Array.

3.19. JB 120

- **Offshore Converter Station Accommodation Barge:** JB 120 has successfully jacked up alongside the East Anglia THREE Offshore Converter Station.
- **Helicopter Operations:** JB120 has conducted personnel transfers via helicopter.

3.20. Centaurus

- **JUB 120 Towing and installation:** Centaurus assisted with the positioning of JB120 alongside the East Anglia THREE Offshore Converter Station.
- **Demobilisation:** Centaurus completed operations and demobilised from the project in the port of Rotterdam on the 11/12/2025.

3.21. Fairplay 62

- **JUB 120 towing and installation:** Fairplay 62 assisted with the positioning of JB120 alongside the East Anglia THREE Offshore Converter Station.
- **Demobilisation:** Fairplay 62 completed operations and demobilised from the project in the port of Rotterdam on the 12/12/2025.

3.22. Esvagt Server

- **JUB 120 towing and installation:** Esvagt Server assisted with the positioning of JB120 alongside the East Anglia THREE Offshore Converter Station.
- **Demobilisation:** Esvagt Server completed operations and demobilised from the project on the 12/12/2025.

3.23. Geo Ocean IV

- **Pre-Installation Survey Campaign:** Geo Ocean IV has continued with Pre-Installation Survey operations within the East Anglia THREE boundary of the Offshore Windfarm Array.
- **Port call:** Geo Ocean IV made a port call to Ijmuiden on the 13/12/2025.

3.24. NKT Victoria

- **Export cable survey:** NKT Victoria has continued with survey operations within the East Anglia THREE export cable corridor.
- **Port call:** NKT Victoria made a port call to Ijmuiden on the 08/12/2025 to conduct a crew change before returning to the East Anglia THREE export cable corridor.

3.25. Esvagt Carpathia

- **Emergency response and rescue vessel:** Esvagt Carpathia has continued providing emergency rescue and recovery support (ERRV) within the East Anglia THREE boundary of the Offshore Windfarm Array.
- **Port call:** Esvagt Carpathia made a port call to Aberdeen on the 13/12/2025.

4. PLANNED OPERATIONS FOR NEXT 7 DAYS

4.1. GV Tess

- **Guard Vessel:** GV Tess will continue with guard vessel duties within the East Anglia THREE boundary of the Offshore Windfarm Array.

4.2. Seaway Ventus

- **Monopile And Transition Piece Installation Campaign:** Seaway Ventus is expected to continue with Monopile and Transition Piece Installation operations within the East Anglia THREE boundary of the Offshore Windfarm Array.
- **Helicopter Operations:** Seaway Ventus will conduct a crew change via helicopter.

4.3. Norside Supporter

- **TP Completion Works:** Norside Supporter will continue with foundation bolting and grouting operations within the East Anglia THREE boundary of the Offshore Windfarm Array.
- **Port call:** Norside Supporter will make a port call to Rotterdam on the 16/12/2025 to complete a crew change before returning to the East Anglia THREE boundary of the Offshore Windfarm Array.

4.4. GV Resolution

- **Export Cable Guard Vessel:** GV Resolution will continue with Guard Vessel duties along the East Anglia THREE export cable corridor.

4.5. GV Accord

- **Export Cable Guard Vessel:** GV Accord will continue with Guard Vessel duties along the East Anglia THREE export cable corridor.

4.6. GV Adventure

- **Export Cable Guard Vessel:** GV Adventure will continue with Guard Vessel duties along the East Anglia THREE export cable corridor.

4.7. GV Arina

- **Export Cable Guard Vessel:** GV Arina will continue with Guard Vessel duties along the East Anglia THREE export cable corridor.

4.8. NR Hunter

- **Crew Transfer Vessel:** NR Hunter will continue with crew transfer duties within the East Anglia THREE boundary of the Offshore Windfarm Array and Export Cable Corridor.

4.9. NR Predator

- **Crew Transfer Vessel:** NR Predator will standby in the port of Lowestoft and be readily available for crew transfer duties within the East Anglia THREE boundary of the Offshore Windfarm Array and export cable corridor.

4.10. NR Rebellion

- **Crew Transfer Vessel:** The NR Rebellion will continue with crew transfer duties within the East Anglia THREE boundary of the Offshore Windfarm Array and Export Cable Corridor.

4.11. Esvagt Cobra

- **Emergency Response and Rescue Vessel:** Esvagt Cobra will continue providing emergency rescue and recovery support (ERRV) within the East Anglia THREE boundary of the Offshore Windfarm Array.

4.12. NKT Victoria

- **Export Cable Survey:** NKT Victoria will continue with survey operations along the East Anglia THREE export cable corridor.
- **Helicopter Operations:** NKT Victoria will conduct a crew change via helicopter.

4.13. Windea Clausius

- **OFCS Platform Commissioning Service Operation Vessel:** Windea Clausius will continue to provide accommodation and Walk-To-Work access for the commissioning phase of the Offshore Converter Station within the East Anglia THREE Offshore Windfarm Array.
- **Demobilisation:** Windea Clausius is expected to complete operations and demobilise from the project.

4.14. Olympic Taurus

- **Post-Lay Mattress Installation:** Olympic Taurus will continue with post-lay mattress installation works along the East Anglia THREE export cable corridor.
- **Port Call:** Olympic Taurus will carry out a port call circa the 18/12/2025 for a planned crew change.

4.15. Bos Prelude

- **OFCS Platform Supply Vessel:** Bos Prelude will continue to perform regular cargo runs between the East Anglia THREE Offshore Converter Station and the ports of Emden, Germany and Lowestoft, UK.

4.16. JB 120

- **Offshore Converter Station Accommodation Barge:** JUB 120 will continue to provide accommodation for the East Anglia THREE Offshore Converter Station (OFCS).
- **Helicopter Operations:** JB 120 will conduct personnel transfers via helicopter.

4.17. Geo Ocean IV

- **Pre-Installation Survey campaign:** Geo Ocean IV will continue with Pre-Installation Survey operations within the East Anglia THREE boundary of the Offshore Windfarm Array.

4.18. Isle of Jura

- **Weather buoy service:** Isle of Jura is expected to return to the East Anglia THREE boundary of the Offshore Windfarm Array circa the 17/12/2025 to conduct weather buoy maintenance.

5. PROJECT CONTACT DETAILS

The following contact can provide relevant information if required. Please note that any specific queries can be addressed to the relevant shore-based representatives.

5.1 SITE MANAGEMENT

Marine Coordinator	
Name	EA3 MCC
Contact Telephone Number	Tel +44 (0) 1416144821
Email Address	ea3_mcc@scottishpower.com
Address	Herring Market, Battery Green Road, Lowestoft, Suffolk, NR32 1BZ

Offshore Installation Manager	
Name	EA3 OIM
Contact Telephone Number	+44 (0) 7960 608 666
Email Address	ea3_oim@scottishpower.com
Address	Herring Market, Battery Green Road, Lowestoft, Suffolk, NR32 1BZ

5.2 EMERGENCY CONTACT

Emergency Contact	
Name	EA3 MCC
Contact Telephone Number	Emergency Tel +44 (0) 1416144822
Email Address	ea3_mcc@scottishpower.com
Address	Herring Market, Battery Green Road, Lowestoft, Suffolk, NR32 1BZ

5.3 MARINE OPERATIONS

Marine Operations	
Name	Anthony Milligan
Contact Telephone Number	Tel +44 (0) 7760 880723
Email Address	amilligan@scottishpower.com
Address	Scottish Power HQ 320 St Vincent Street, Glasgow, G2 5AD

6. INSTALLATION PROGRESS

The following table shows the East Anglia THREE planned installation locations and status

ID	Structure	Latitude	Longitude	Jacket Installed	Topside Installed	Light Characteristic
OFCS	Offshore Converter Station	52° 40.242' N	002° 51.763' E	11/08/2025	16/10/2025	FL Y 2.5s light 360° Range 2nm.

ID	Structure	Latitude	Longitude	MP Installed	TP Installed	Light Characteristic
A02	WTG	52° 32.196' N	002° 45.780' E	N	N	
A03	WTG	52° 32.804' N	002° 45.748' E	N	N	
A04	WTG	52° 33.437' N	002° 45.773' E	N	N	
A05	WTG	52° 34.057' N	002° 45.770' E	N	N	
A06	WTG	52° 34.677' N	002° 45.767' E	N	N	
A07	WTG	52° 35.319' N	002° 45.740' E	N	N	
A08	WTG	52° 35.918' N	002° 45.760' E	N	N	
A09	WTG	52° 36.551' N	002° 45.756' E	N	N	
A10	WTG	52° 37.169' N	002° 45.765' E	11/12/2025	11/12/2025	FL Y 2.5s light 360° Range 2nm.
A11	WTG	52° 37.779' N	002° 45.750' E	21/11/2025	21/11/2025	FL Y 2.5s light 360° Range 2nm.
A12	WTG	52° 38.399' N	002° 45.747' E	09/11/2025	10/11/2025	FL Y 2.5s light 360° Range 2nm.
A14	WTG	52° 39.640' N	002° 45.740' E	N	N	
A15	WTG	52° 40.260' N	002° 45.737' E	N	N	
A16	WTG	52° 40 880' N	002° 45.733' E	N	N	
A17	WTG	52° 41 500' N	002° 45 729' E	23/09/2025	23/09/2025	FL Y 2.5s light 360° Range 2nm.
A18	WTG	52° 42.121' N	002° 45.727' E	19/06/2025	20/06/2025	FL Y 2.5s light 360° Range 2nm.
A19	WTG	52° 42.741' N	002° 45.723' E	01/09/2025	01/09/2025	FL Y 2.5s light 360° Range 2nm.
B01	WTG	52° 31.688' N	002° 48.252' E	N	N	
B02	WTG	52° 32.332' N	002° 48.231' E	N	N	
B03	WTG	52° 32.943' N	002° 48.176' E	N	N	
B04	WTG	52° 33.563' N	002° 48.137' E	N	N	
B05	WTG	52° 34.151' N	002° 48.071' E	N	N	
B06	WTG	52° 34 802' N	002° 48 061' E	N	N	
B07	WTG	52° 35.436' N	002° 48.022' E	N	N	
B08	WTG	52° 36.043' N	002° 47.984' E	N	N	
B09	WTG	52° 36.662' N	002° 47.945' E	N	N	
B10	WTG	52° 37.282' N	002° 47.908' E	29/04/2025	30/04/2025	FL Y 2.5s light 360° Range 2nm.
B11	WTG	52° 37.892' N	002° 47.831' E	N	N	
B12	WTG	52° 38.521' N	002° 47.830' E	02/11/2025	03/11/2025	FL Y 2.5s light 360° Range 2nm.
B14	WTG	52° 39.761' N	002° 47.753' E	N	N	
B15	WTG	52° 40.381' N	002° 47.715' E	N	N	

B16	WTG	52° 41.002' N	002° 47.677' E	13/07/2025	13/07/2025	FL Y 2.5s light 360° Range 2nm.
B17	WTG	52° 41.621' N	002° 47.637' E	28/09/2025	29/09/2025	FL Y 2.5s light 360° Range 2nm.
B18	WTG	52° 42.241' N	002° 47.599' E	06/07/2025	07/07/2025	FL Y 2.5s light 360° Range 2nm.
B19	WTG	52° 42.861' N	002° 47.561' E	21/05/2025	22/05/2025	FL Y 2.5s light 360° Range 2nm.
B20	WTG	52° 43.481' N	002° 47.522' E	09/06/2025	09/06/2025	FL Y 2.5s light 360° Range 2nm.
B21	WTG	52° 44.123' N	002° 47.482' E	13/07/2025	15/07/2025	FL Y 2.5s light 360° Range 2nm.
C03	WTG	52° 33.093' N	002° 50.760' E	N	N	
C04	WTG	52° 33.708' N	002° 50.671' E	N	N	
C06	WTG	52° 34.944' N	002° 50.493' E	18/04/2025	18/04/2025	FL Y 2.5s light 360° Range 2nm.
C07	WTG	52° 35.562' N	002° 50.404' E	N	N	
C08	WTG	52° 36.180' N	002° 50.314' E	N	N	
C11	WTG	52° 38.034' N	002° 50.046' E	N	N	
C12	WTG	52° 38.651' N	002° 49.956' E	N	N	
C13	WTG	52° 39.269' N	002° 49.867' E	04/12/2025	05/12/2025	FL Y 2.5s light 360° Range 2nm.
C15	WTG	52° 40.505' N	002° 49.687' E	N	N	
C16	WTG	52° 41.102' N	002° 49.570' E	29/06/2025	30/06/2025	FL Y 2.5s light 360° Range 2nm.
C17	WTG	52° 41.741' N	002° 49.508' E	14/10/2025	15/10/2025	FL Y 2.5s light 360° Range 2nm.
C18	WTG	52° 42.359' N	002° 49.417' E	07/10/2025	07/10/2025	FL Y 2.5s light 360° Range 2nm.
C19	WTG	52° 42.976' N	002° 49.328' E	09/09/2025	10/09/2025	FL Y 2.5s light 360° Range 2nm.
C20	WTG	52° 43.595' N	002° 49.238' E	19/10/2025	19/10/2025	FL Y 2.5s light 360° Range 2nm.
C21	WTG	52° 44.213' N	002° 49.148' E	01/07/2025	02/07/2025	FL Y 2.5s light 360° Range 2nm.
D06	WTG	52° 35.087' N	002° 52.463' E	N	N	
D07	WTG	52° 35.695' N	002° 52.362' E	N	N	
D08	WTG	52° 36.313' N	002° 52.280' E	21/04/2025	22/04/2025	FL Y 2.5s light 360° Range 2nm.
D09	WTG	52° 36.932' N	002° 52.199' E	N	N	
D10	WTG	52° 37.550' N	002° 52.118' E	26/05/2025	27/05/2025	FL Y 2.5s light 360° Range 2nm.
D11	WTG	52° 38.168' N	002° 52.037' E	N	N	
D12	WTG	52° 38.786' N	002° 51.955' E	N	N	
D13	WTG	52° 39.405' N	002° 51.874' E	02/05/2025	03/05/2025	FL Y 2.5s light 360° Range 2nm.
D15	WTG	52° 40.640' N	002° 51.696' E	10/10/2025	10/10/2025	FL Y 2.5s light 360° Range 2nm.
D16	WTG	52° 41.258' N	002° 51.592' E	N	N	
D17	WTG	52° 41.874' N	002° 51.486' E	30/09/2025	30/09/2025	FL Y 2.5s light 360° Range 2nm.
D18	WTG	52° 42.492' N	002° 51.382' E	13/12/2025	13/12/2025	FL Y 2.5s light 360° Range 2nm.
D19	WTG	52° 43.108' N	002° 51.276' E	24/09/2025	25/09/2025	FL Y 2.5s light 360° Range 2nm.
D20	WTG	52° 43.726' N	002° 51.172' E	06/09/2025	06/09/2025	FL Y 2.5s light 360° Range 2nm.

D21	WTG	52° 44.343' N	002° 51.067' E	11/06/2025	11/06/2025	FL Y 2.5s light 360° Range 2nm.
E10	WTG	52° 37.691' N	002° 54.697' E	N	N	
E11	WTG	52° 38.317' N	002° 54.545' E	N	N	
E12	WTG	52° 38.982' N	002° 54.439' E	N	N	
E13	WTG	52° 39.571' N	002° 54.296' E	N	N	
E15	WTG	52° 40.799' N	002° 54.010' E	N	N	
E16	WTG	52° 41.413' N	002° 53.867' E	14/09/2025	14/09/2025	FL Y 2.5s light 360° Range 2nm.
E20	WTG	52° 43.870' N	002° 53.293' E	21/06/2025	22/06/2025	FL Y 2.5s light 360° Range 2nm.
E21	WTG	52° 44.487' N	002° 53.108' E	09/07/2025	09/07/2025	FL Y 2.5s light 360° Range 2nm.
F13	WTG	52° 39.712' N	002° 56.434' E	N	N	
F14	WTG	52° 40.328' N	002° 56.320' E	N	N	
F15	WTG	52° 40.945' N	002° 56.206' E	07/12/2025	08/12/2025	FL Y 2.5s light 360° Range 2nm.
F16	WTG	52° 41.561' N	002° 56.092' E	N	N	
F17	WTG	52° 42.178' N	002° 55.978' E	16/10/2025	16/10/2025	FL Y 2.5s light 360° Range 2nm.
F18	WTG	52° 42.791' N	002° 55.906' E	N	N	
F19	WTG	52° 43.411' N	002° 55.750' E	N	N	
F20	WTG	52° 44.027' N	002° 55.636' E	N	N	
F21	WTG	52° 44.644' N	002° 55.522' E	N	N	
F22	WTG	52° 45.260' N	002° 55.408' E	06/11/2025	06/11/2025	FL Y 2.5s light 360° Range 2nm
G16	WTG	52° 41.699' N	002° 58.142' E	N	N	
G17	WTG	52° 42.315' N	002° 58.029' E	N	N	
G19	WTG	52° 43.535' N	002° 57.802' E	N	N	
G20	WTG	52° 44.164' N	002° 57.689' E	N	N	
G21	WTG	52° 44.781' N	002° 57.575' E	N	N	
G22	WTG	52° 45.398' N	002° 57.461' E	N	N	
H19	WTG	52° 43.685' N	002° 59.854' E	N	N	
H20	WTG	52° 44.264' N	002° 59.756' E	N	N	
H21	WTG	52° 44.902' N	002° 59.648' E	N	N	
H22	WTG	52° 45.535' N	002° 59.515' E	N	N	
			TOTAL:	37/95	37/95	

7. VESSEL DETAILS

Vessel Details		
Name of Vessel:	Tess	
Call Sign:	T7AH7	
MMSI No:	2682239102	
Contact Details:	Phone: +31 255 760 071 Email: tess@dbconnect.nl	

Vessel Details		
Name of Vessel:	Seaway Ventus	
Call Sign:	5BFU6	
MMSI No:	209583000	
Contact Details:	Phone: + 31 6 535 46 853 Email: Seawayventus.bridge@seaway7.com	

Vessel Details		
Name of Vessel:	Norside Supporter	
Call Sign:	C6GP4	
MMSI No:	311001311	
Contact Details:	Phone: +47 46701233 Email: master.supporter@stodig.no	

Vessel Details		
Name of Vessel:	Reul Na Mara	
Call Sign:	GGKA	
MMSI No:	234671000	
Contact Details:	Phone: +44(0)1449700236 Email: gvreulnamara@gmail.com	

Vessel Details		
Name of Vessel:	GV Adventure	
Call Sign:	2IFE4	
MMSI No:	235109237	
Contact Details:	Phone: +44 (0) 1947750717 Email: gvadventure3@gmail.com	

Vessel Details		
Name of Vessel:	GV Arina	
Call Sign:	MVM7	
MMSI No:	234002000	
Contact Details:	Phone: +44 (0) 1346 410 489 Email: gvarinalk80@gmail.com	

Vessel Details		
Name of Vessel:	GV Resolution	
Call Sign:	MBCZ5	
MMSI No:	235002260	
Contact Details:	Phone: +44 19 4766 0301 Email: gvresolution@gmail.com	

Vessel Details		
Name of Vessel:	GV Accord	
Call Sign:	2WEM	
MMSI No:	234219000	
Contact Details:	Phone: 008821644447327 Email: gvaccordn262@gmail.com	

Vessel Details		
Name of Vessel:	GV Renown	
Call Sign:	MEX09	
MMSI No:	232021109	
Contact Details:	Phone: +44 28 4114 0716 Email: renownn1063@gmail.com	

Vessel Details		
Name of Vessel:	NKT Victoria	
Call Sign:	LAWV7	
MMSI No:	257016000	
Contact Details:	Phone: +47(0) 224 08110 Email: bridge.victoria@remoy-management.no	

Vessel Details		
Name of Vessel:	NR Hunter	
Call Sign:	MROM5	
MMSI No:	232059247	
Contact Details:	Phone: +44(0)7944974021 Email: hunter@nrmarine.co.uk	

Vessel Details		
Name of Vessel:	NR Rebellion	
Call Sign:	MROM4	
MMSI No:	232059246	
Contact Details:	Phone: +44 (0) 7984321461 Email: rebellion@nrmarine.co.uk	

Vessel Details		
Name of Vessel:	NR Predator	
Call Sign:	MOTT9	
MMSI No:	232053207	
Contact Details:	Phone: 07398653457 Email: predator@nrmarine.co.uk	

Vessel Details		
Name of Vessel:	Olympic Taurus	
Call Sign:	LDXA3	
MMSI No:	257959000	
Contact Details:	Phone: +49 1520 4827535 Email: taurus.bridge@olympic.no	

Vessel Details		
Name of Vessel:	JUB 120	
Call Sign:	C6IE5	
MMSI No:	311001648	
Contact Details:	Phone: +31 162 762 672 Email: ro120@jackupbarge.com	

Vessel Details		
Name of Vessel:	Flintstone	
Call Sign:	PBZD	
MMSI No:	245861000	
Contact Details:	Phone: +49 421 517 2191 96 3 Email: captain.flintstone@ships.deme-group.com	

Vessel Details		
Name of Vessel:	WINDEA Clausius	
Call Sign:	CQ2750	
MMSI No:	255916481	
Contact Details:	Phone: +49 1520 4827535 Email: bridge@windea.clausius.bsmfleet.com	

Vessel Details		
Name of Vessel:	Bos Prelude	
Call Sign:	PBZK	
MMSI No:	253000039	
Contact Details:	Phone: +447957302781 Email: bridge.prelude@ship.britoil.com.sg	

Vessel Details		
Name of Vessel:	Centaurus	
Call Sign:	V2ED3	
MMSI No:	305820000	
Contact Details:	Email: imo9433755@marlowfleet.com Sat Phone: +494 067 529 190 Phone: +31 689 927 402	

Vessel Details	
Name of Vessel:	Fairplay 62
Call Sign:	DDBC2
MMSI No:	211876000
Contact Details:	Email: fairplay-62@fairplay-towage.com Phone: +49 160 963 556 90 Sat Phone: +870 773 166 325



Vessel Details	
Name of Vessel:	Esvagt Server
Call Sign:	OWKK2
MMSI No:	219449000
Contact Details:	Email: server.master@esvagtvesel.com Phone: +45 61 626 776



Vessel Details	
Name of Vessel:	Esvagt Cobra
Call Sign:	Ouka2
MMSI No:	219009000
Contact Details:	Phone: +45 21 778 895 Email: cobra@esvagtvesel.com



Vessel Details	
Name of Vessel:	Esvagt Carpathia
Call Sign:	OXRZ2
MMSI No:	219009417
Contact Details:	Phone: +881 64170 6781 Email: carpathia@esvagtvesel.com



Vessel Details		
Name of Vessel:	Isle of Jura	
Call Sign:	MFFY6	
MMSI No:	232021966	
Contact Details:	Phone: +44 (0) 7936910623 Email: Jura@seafastltd.co.uk	

Vessel Details		
Name of Vessel:	Grand Canyon III	
Call Sign:	LACJ8	
MMSI No:	257010590	
Contact Details:	Phone: +87 07 73 20 47 49 Email: master@grand-canyon.no	
